

NOTE WATER PROOFING ON WALL TO BE DONE UP TO 600 MM HEIGHT FROM UNFINISHED FLOOR LEVEL


AHMEDABAD DWG No			LOCATION	HS	
-	DWG.No.	PRAKASH 2023-11-21 PRAKASH	DRAWN BY	SHEET DETAIL	
		2023-11-21	DATE	٦	
NTS	SCALE	PRAKASH	СНК ВҮ	≥	
			DATE	l Dimens	
	REVISION DATE	RO	LOCATION DRAWN BY DATE CHK BY DATE REVISION No. OPERATIONS	All Dimensions Are In MM	
SIGN		DATE	OPER		
			ATIONS		
(	NGN NGN	DATE	CHEF		
			Hi		
SIGN		DATE	PRO	WA	
			PROJECTS	WATER PROOFING - LAYOU	
01014	0	DATE	FIRE	3 - LAYOU	

PROJECT

THIRD WAVE COFFEE

## WATER PROOFING METHODOLOGY

- 1. Removal of Top Screed from the Mother Slab
- 2. Cleaning of the Mother Slab with Hard Brush & Removal of Dirt from the Surface with Air Blowers
- 3. Applying of the Fosroc RFX Brush Bond Coating on the mother slab with Brush in Clock wise directions & on all 4 Sides Walls till 1200m in Height. If the Floor is raised 300m.m
- 4. After drying of the 1st Coat of the Brush Bond Coating, 2nd Coat is applied in the Anticlockwise
- 5. After drying of entire Surface say 24 Hours we will fill Water to 6 inch Levels for Ponding Testing
- 6. Water will be kept for observations for 72 Hours. If Leakage is observed. Water is emptied
- Above Procedure is Repeated.
- 8. If No Leakage is observed after 72 Hours. Water will be drained out from the Floor Surface
- 9. Protective Screeding mixed with FOSROC NITOBOND SBR of Average 25m.m thickness will be laid
- 10. After Dryings of Protective Screed say 2 Days. Drain Lines are laid on the Floor with Slope above water Proofing Surface with coving & Wall junction.
- & main Drain lines chambers are done
- 12. After this floor raising by Light Seaproax block will be achieved followed with flooring material as

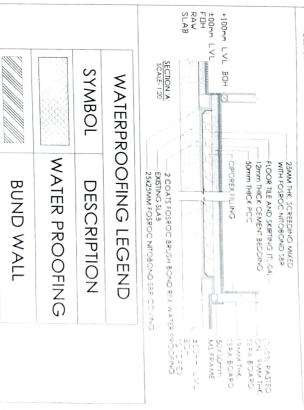

SIGN	DATE	PROJECTS	WATER PROC
SIGN	DATE	FIRE OFFICER	WATER PROOFING - LAYOUT
SIGN	DATE	000	INHOUSE DESIGN
