

column

Remove wall & 4 vertical

- 1) Door Remove.
- 2) Water pipe Remove & Draining.
- 3) Service room tile Remove.


5/12/2023

Prakash
5/12/2023



WATER PROOFING METHODOLOGY:

1. Removal of Top Screed from the Mother Slab.
2. Cleaning of the Mother Slab with Hard Brush & Removal of Dirt from the Surface with Air Blowers
3. Applying of the Fosroc RFX Brush Bond Coating on the mother slab with Brush in Clock wise directions & on all 4 Sides Walls till 1200mm.m Height. If the Floor is raised 300mm.m
4. After drying of the 1st Coat of the Brush Bond Coating, 2nd Coat is applied in the Anticlockwise Directions
5. After drying of entire Surface say 24 Hours, we will fill Water to 6 Inch Levels for Ponding Testing.
6. Water will be kept for observations for 72 Hours. If Leakage is observed, Water is emptied
7. Above Procedure is Repeated.
8. If No Leakage is observed after 72 Hours, Water will be drained out from the Floor Surface.
9. Protective Screeding mixed with FOSROC NITOBOND SBR of Average 25mm thickness will be laid above water Proofing Surface with coving & Wall junction.
10. After Drying of Protective Screed say 2 Days, Drain Lines are laid on the Floor with Slope & main Drain lines chambers are done.
12. After this floor raising by Light Seaprox block will be achieved followed with flooring material as desired.

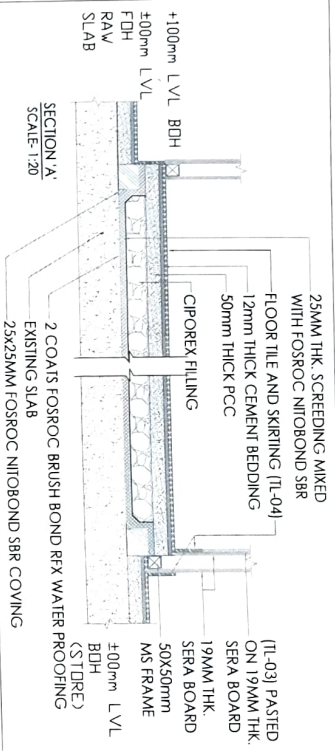

WATERPROOFING LEGEND	
SYMBOL	DESCRIPTION
	WATER PROOFING
	BUND WALL

NOTE WATER PROOFING ON WALL TO BE DONE UP TO 600 MM HEIGHT FROM UNFINISHED FLOOR LEVEL.

SHEET DETAIL All Dimensions Are In MM

PROJECT	LOCATION	DRAWN BY	DATE	CHK BY	DATE	REVISION No.	OPERATIONS	CHEF	PROJECTS	FIRE OFFICER	COO
KFC	AHMEDABAD	PRAKASH	2023-11-21	PRAKASH		R0					
	T1	DWG No.		SCALE		REVISION DATE	DATE	DATE	DATE	DATE	DATE
				NTS			SIGN	SIGN	SIGN	SIGN	SIGN

WATER PROOFING - LAYOUT INHOUSE DESIGN
